

# ELIZABETH LINE COMMITTEE: DASHBOARD

Data date: 23-Dec-21

## READER GUIDANCE:

### HEALTH AND SAFETY

- A High Potential Near Miss (HPNM) is an incident that could have caused a significant injury but that did not in this instance.
- A Lost Time Case (LTC) is an incident that resulted in an individual or individuals suffering an injury that necessitated time off from working.
- A RIDDOR is an incident that is reportable under the RIDDOR 2013 regulations. For more detail on what is reportable, [click here](#) for the Health and Safety Executive guidance page.
- Health and Safety Performance Index (HSPI) is an aggregated contractual measure of contractor compliance with Crossrail's Golden Rules.

### MILESTONE FORECAST SCENARIOS


- Forecast scenario dates are derived through the 4-weekly schedule and risk updates, with quantitative risk modelling building the P50 and P80 Scenario Dates. Note, these do not include any risk to the Trial Operations period.
- The table identifies the earliest possible dates before risk assessment which is derived from the shortest path to completion, and the P50 and P80 dates (i.e. the date by which, through risk modelling, a milestone is achieved 50% of the time and 80% of the time respectively).

### ACTIVITY SEQUENCING TO STAGE 3 REVENUE SERVICE


- It has been agreed that a two phase Trial Operations approach is to be undertaken. This resulted in a new Trial Operations Phase 2 milestone set for January 2022 and a re-forecast of Stage 3A Revenue Service to March 2022.

## 1. HEALTH AND SAFETY


### Lost Time Cases




### RIDDOR (Reportable Incidents)



### High Potential Near Misses



### H&S Performance Index




## 2. KEY MILESTONES – FORECAST SCENARIOS (BASED ON PERIOD 09 FY21/22 DATA)

Note: This forecast and performance to date aligns to the P50 Scenario Date that informed the August 2020 announcement that Crossrail expects the Elizabeth line to open within the first half of 2022.

Milestone	Earliest Date (Period 02 FY21/22)	P50 Scenario Date	P80 Scenario Date
Transition to a ROGS Environment		ACHIEVED – 27 March 2021	
Trial Running (with 4TPH) - Start		ACHIEVED – 10 May 2021	
Trial Operations Phase 1 - Start		ACHIEVED – 20 November 2021	
Trial Operations Phase 2 - Start	January 2022	February 2022	March 2022
Commencement of Stage 3 Revenue Service	March 2022	May 2022	June 2022

## 3. KEY ACHIEVEMENTS AND ACTIVITY SEQUENCING TO STAGE 3 REVENUE SERVICE

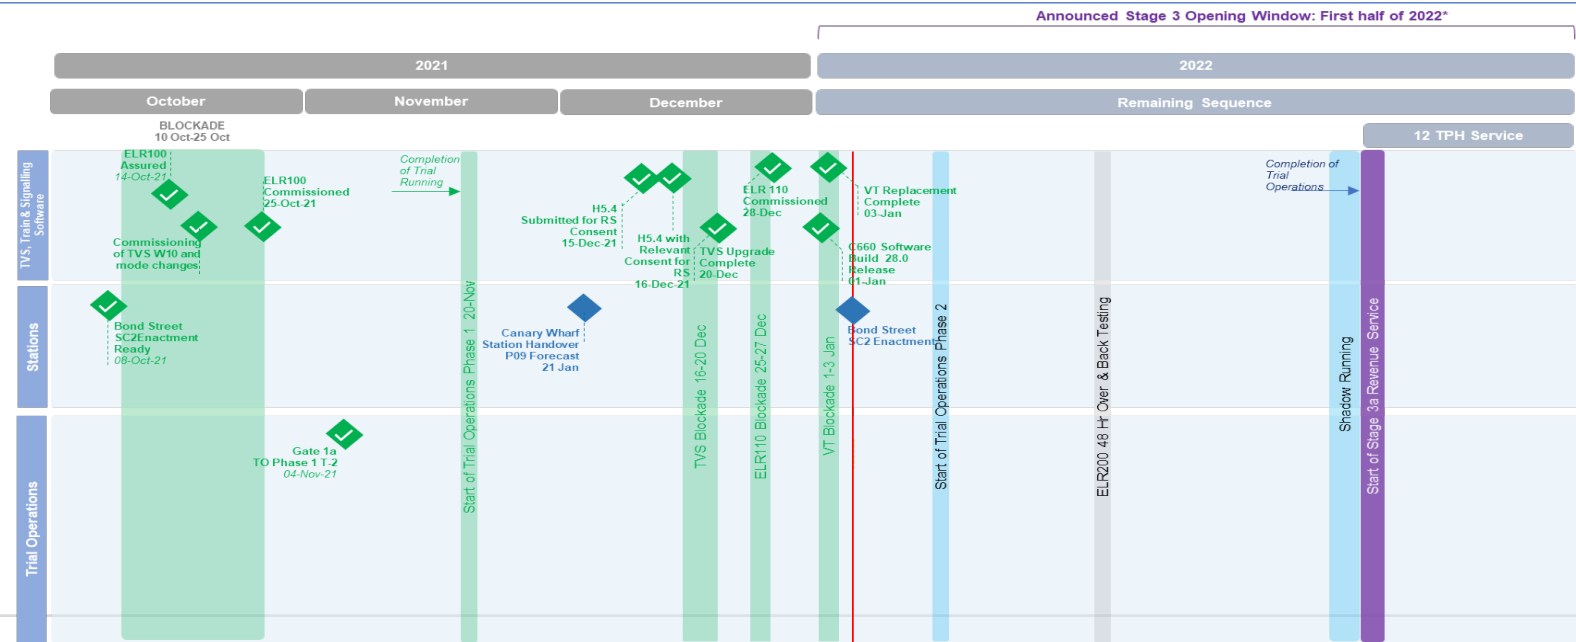

\*Note: this is the sequence and is not reflective of timings
